

Guidebook for

SITE MANAGEMENT PLATFORMS

Pre-release

Part A – For Solution Providers

Published Apr 2024



Acknowledgements

BCA would like to acknowledge the contributions of the following organisations which had provided their valuable inputs in the development of the Guidebook.

- Arth Design Build Pte Ltd
- Autodesk Asia Pte. Ltd.
- BES Global Pte. Ltd.
- BIMAGE Consulting Pte. Ltd.
- Boustead Projects Pte Ltd
- Chan Rong Fen Building Construction Pte Ltd
- China Communications Construction Company Ltd
- China Construction (South Pacific) Development Co Pte Ltd
- Housing & Development Board (HDB)
- Hubble.Build
- Infocomm Media Development Authority (IMDA)
- Intercorp Solutions Pte Ltd
- JTC Corporation
- Lean Station Pte Ltd
- Magicsoft Asia Systems Pte Ltd
- Novade Solutions Pte. Ltd.
- Oracle Corporation Singapore Pte Ltd
- PlanRadar Singapore Pte Ltd.
- Precise Development Pte Ltd
- Singapore Trade Data Exchange (SGTradex) Technologies Pte. Ltd.
- Straits Construction Singapore Pte Ltd

Disclaimer

This Guide is a summary of practices and recommendations that may be adopted for the application of Site Management Platform (SMPs) and does not purport to be exhaustive or applicable to all situations.

The Building and Construction Authority (BCA) disclaims any liability (including any liability arising from negligence) arising in respect of any matter and the consequences of any act done or not done by any person in reliance on anything in or omitted from this Guide.

This Guide may be amended from time to time. Please refer to the website of the Building and Construction Authority (BCA): www.bca.gov.sg for the latest version of this Guide.

©Copyright

We extend our special thanks to the solution providers* below for their valuable contribution of photos and materials in this publication. Their collaboration has significantly enriched the content. The photos and infographics in this publication are protected by copyright law. Any unauthorised use, reproduction, or distribution of the photographs is strictly prohibited.

* Includes list of solution providers

Table of Contents


INTRODUCTION	5
Definition of Site Management Platforms	5
Common Data Environment	5
PART 1. OBJECTIVES OF SITE MANAGEMENT PLATFORMS	6
1.1 Work Productivity	6
1.2 Construction Structural and Workplace Safety	7
1.3 Site Supervision	8
1.4 Improved Data Accuracy and Document Management	8
1.5 Quality Performance and Data Analytics	8
1.6 Audit Trail	8
PART 2. FUNCTIONAL REQUIREMENTS OF SITE MANAGEMENT PLATFORMS	9
2.1 Form and Data Requirements	9
2.2 Form and Data Management	10
2.3 Workflow and Report Management	11
2.4 Essential Functions	12
2.5 User Management	12
2.6 Smart Site Sensors Management	13
PART 3. OTHER OPERATIONAL REQUIREMENTS	14
3.1 IT Security Requirements	14
3.2 Connection to Exchange Platform	14
3.3 System Maintenance	15
3.4 Archiving of Data After Project Completion	15

1 INTRODUCTION

Definition of Site Management Platforms

The construction process, from start to finish, entails complex procedures that result in the constant production, collection and management of data at the construction site. Site Management Platforms (SMPs) serve as a centralised digital hub to collect and consolidate such construction works information and data. Through SMPs, project parties can efficiently communicate and share information, facilitating seamless flow of data across the construction project.

Examples of data that can be stored on Site Management Platforms

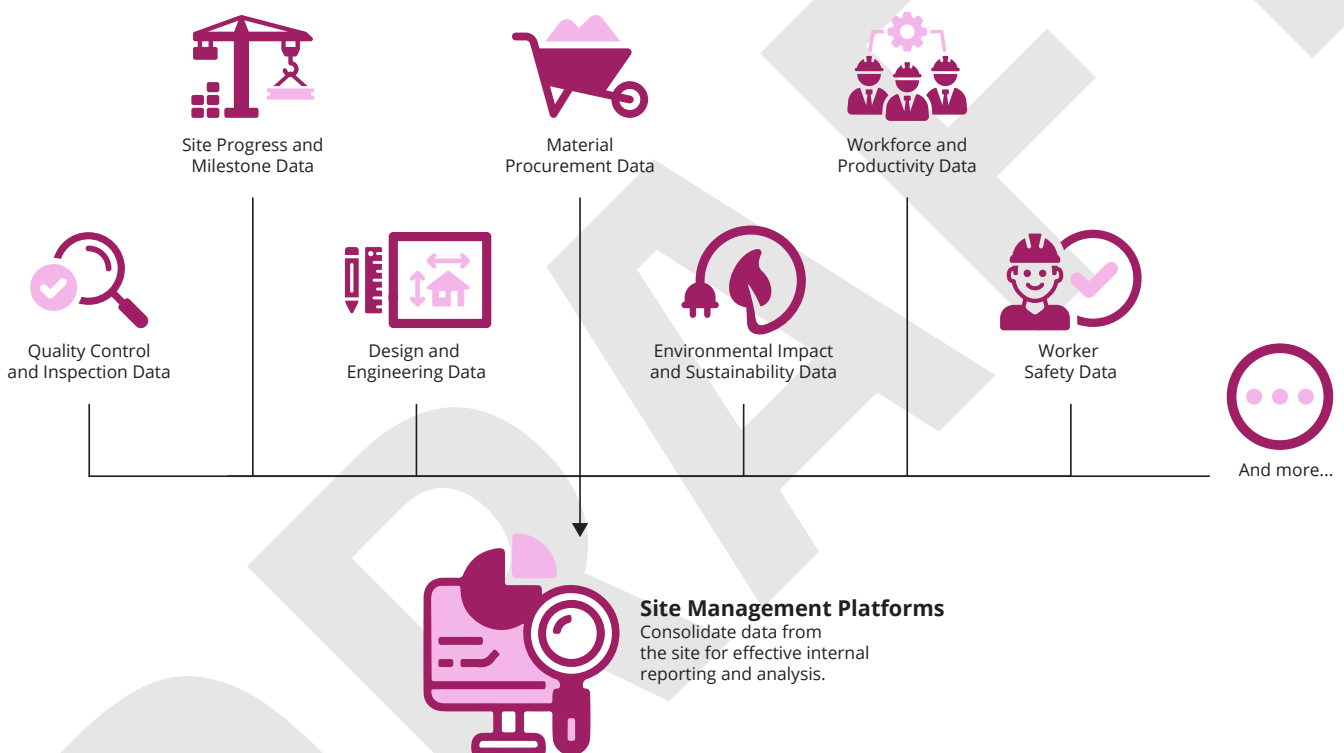

This Guide is intended to help solution providers set up SMPs for BCA regulatory use cases, which includes basic functional requirements, recommended workflows for digital management of essential site and test records. Other project parties including Developers, Builders, Site Supervisors, Supervising Qualified Persons (as defined in the Building Control Act 1989) (“Supervising QPs”) may also refer to this Guide to work with solution providers for SMP adoption.

Common Data Environment

The adoption of a Common Data Environment (CDE) is pivotal in streamlining collaboration and information management for a construction project. The CDE serves as a unified platform for storing, sharing, and accessing project data, promoting transparency and efficiency across the construction life cycle. The SMPs can form part of the CDE, when connected through an Application Programming Interface (API). This will then enable seamless sharing of construction site data among project stakeholders, thereby enhancing overall project coordination and delivery.

PART 1

OBJECTIVES OF SITE MANAGEMENT PLATFORMS

Digitalisation and technology have brought about numerous benefits to the entire lifecycle of construction projects. For instance, it can save time in the field by enabling one-time data collection for use within the team, and facilitate the monitoring of daily site work progress at the project office as well as global operations performance at the headquarters.

Adopting SMPs as the digital platform for collecting construction site data offers benefits for various parties:

- Stakeholders
- General and specialist contractors
- Architects
- Engineers
- Facility and property managers
- Consultants
- And more




SMPs can be applied in various ways within the construction industry as the digital platform to collect construction site data and manage the workflows of site activities. Users can utilise the captured data to monitor and report work progress. Such timely reporting and alerts of work progress can enhance work productivity, workplace safety, and quality performance. Examples of the diverse applications of SMP include, but are not limited to the following, listed below.

Work Productivity


SMPs can assist in managing equipment and resources efficiently. By using an SMP to monitor daily site records, deployment of resources such as site workers, materials, transportation etc., can be improved and arranged in advance. SMPs help to provide visibility of resource availability and optimise resource allocation to reduce wastage and increase productivity.

In addition, proper planning for site activities can help to reduce operational costs. SMPs can be used to better manage project schedules, task assignments and track progress to ensure the timely completion of tasks, reducing downtime.

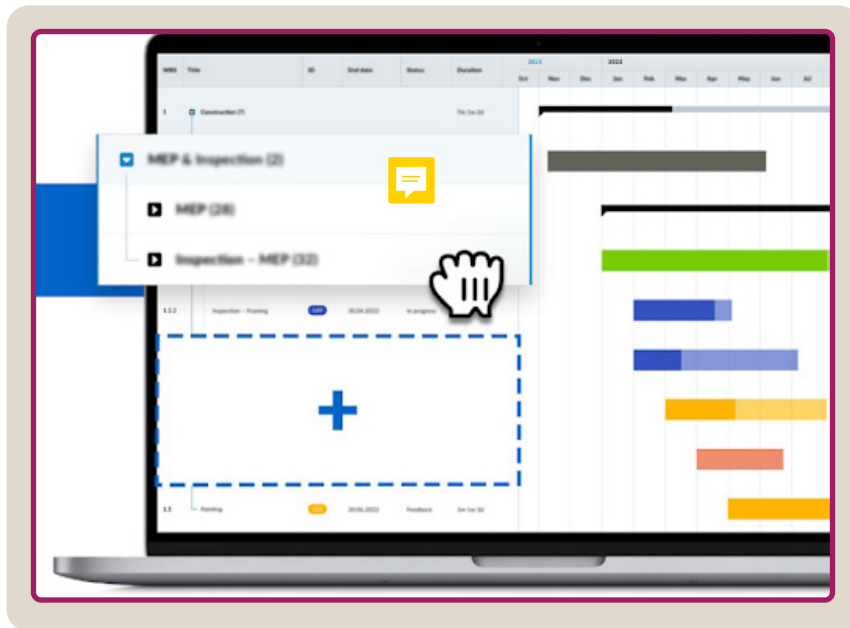

Construction Structural and Workplace Safety

SMPs can play a crucial role in improving structural safety at construction sites through the proper documentation of site records. They achieve this by enabling the effective tracking of structural elements, adherence to the approved plan and the implementation of proactive measures to maintain quality of works and structural integrity. SMPs can also be used for work accident reporting, ensuring prompt attention and investigation. Using SMPs to track safety incidents and near-misses can help to identify trends, implement corrective actions and prevent similar incidents in the future. This then allows supervisors to better conduct safety inspections and audits, thereby promoting a culture of proactive safety management and compliance with regulations.

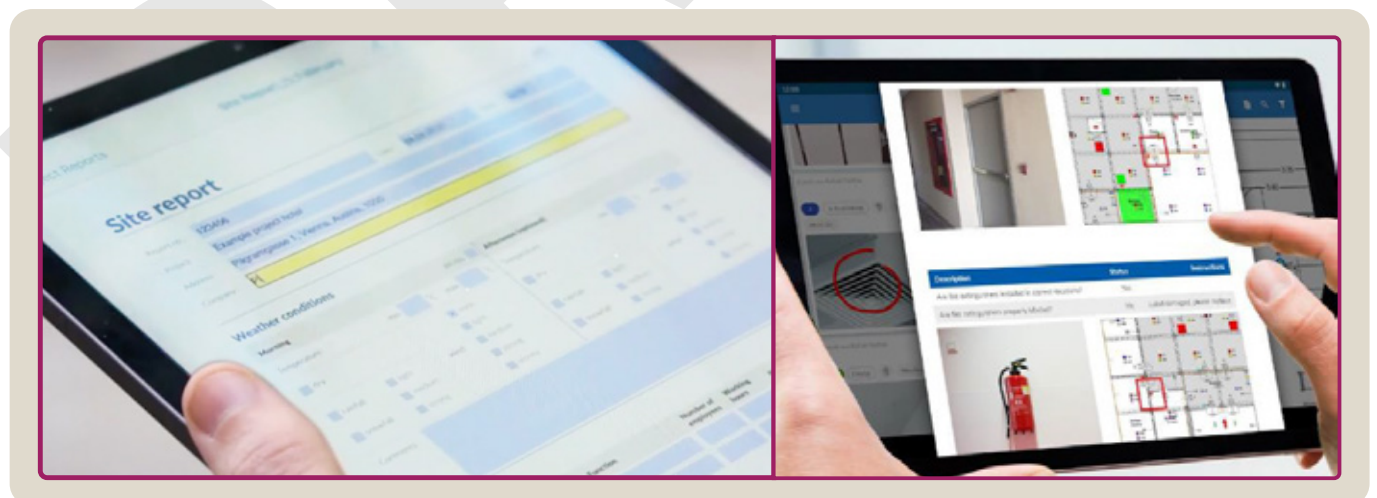

Site Supervision

SMPs can also greatly improve site supervision for Qualified Persons (QPs) by enhancing their oversight, and enabling them to remotely monitor construction activities, assign tasks, communicate with the team, manage documents, and generate reports for informed decision-making.

Improved Data Accuracy and Document Management

SMPs provide a standardised template for data entry, ensuring consistency and accuracy across different records. Using SMPs as a centralised repository for storing and managing project documents will also reduce the chances of referencing incorrect or outdated information.

Quality Performance and Data Analytics

Consistent use of SMPs to collect data over time will allow for data analytics. This will enable users to identify trends, take immediate actions to solve issues and improve the quality of performance.




Audit Trail

SMPs often offer version control and an audit trail feature, allowing users to track changes made to the records over time. This helps in identifying who made the changes and when, ensuring accountability and transparency.

Note: This Guidebook focuses on data collection related to structural safety.

While SMPs can be used in many ways, the primary focus for this Guidebook is outlining necessary modules for collecting data related to structural safety to serve the needs for BCA as regulators. This Guidebook will not detail specific requirements for use-cases beyond structural safety. Solution providers should consult with their clients on their additional needs or provide additional modules/fields to value-add and meet their client's specific requirements.

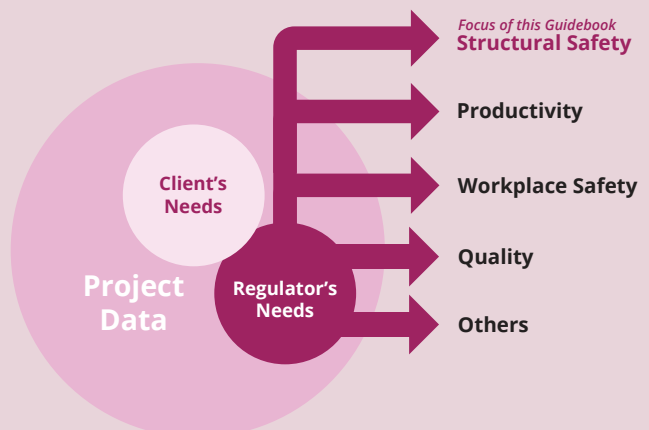

PART 2

FUNCTIONAL REQUIREMENT OF SMPs

Form and Data Requirements

This section covers the required structured and unstructured data as well as optional data to be collected in SMPs.

Structured data refers to organised and formatted information that is readily identifiable and searchable. It is typically presented in a well-defined and predictable format, often using rows and columns, making it easy for machines to interpret and process. This structured format allows for efficient storage, retrieval, and analysis of the data, enabling automated processing and analysis. Examples of structured data include data in relational databases, spreadsheets, and standardised file formats such as CSV (Comma-Separated Values) and JSON (JavaScript Object Notation).

Unstructured data refers to information that does not have a predefined data model or is not organised in a pre-defined manner. This type of data does not fit neatly into traditional databases or spreadsheets and lacks a specific structure, making it more challenging to analyse using conventional methods. Unstructured data can include text documents, images, audio files, video files, social media posts, and other forms of content that do not have a fixed format.

Required (Compulsory datasets for projects adopting SMPs)			
(A) Structured Data		(B) Unstructured Data	
A1	QP/SS Attendance Record	B1	Pre-con Survey Report
A2	Site Investigation Report	B2	Temporary Building Design (COS, PE Design & Layout plans)
A3	Pile Load Test	B3	Steel Mill Cert & FPC
A4	Piling Installation Record	B4	Welding Test Report
A5	Instrumentation & Monitoring	B5	QP(D) Approval for Proprietary Product
A6	ERSS Annex C-1: Site Inspection & Approval Records	B6	360 Captures
A7	Annex D: Certification of Monitoring Building Settlement	B7	Original Reports for structured datasets (if necessary)
A8	Concrete Cube Test Results	B8	BCA Permit to carry out structural work*
A9	Steel Strength Test Results	B9	BCA Approved drawings/Amendment plans*
A10	Generic Notification Module	B10	Site Supervision Plan
A11	Site Progress		
A12	MET Test Results (finger joint, delamination, bending and shear test)		

Table 1: List of required data

*Documents are issued by BCA and will be required to be kept on SMP for project's own reference

No part of this document may be produced or copied on any form or by any means without BCA's prior permission.

Optional data refers to information that is not mandated by BCA for storage in SMPs. However, it represents a valuable filing practice that facilitates efficient data processing, analysis, and reporting, ultimately leading to time and resource savings.

Optional (Good to have and implement in SMPs)	
C1	RFI Forms
C2	Inspection Checklists (as stated in Site Supervision Guidebook)
C3	Schedule of Works
C4	Information of piling machines (including calibration records)
C5	Images of soil condition/rocks
C6	Records of point load test for rocks
C7	Shop drawings & approval from Qualified Person
C8	Construction drawings (issued by Qualified Person)
C9	Method of statements/construction sequence
C10	Post-tensioning records (elongation calculated and measured)
C11	Grouting records
C12	Appointment of Specialist Builder/Professional Engineer
C13	Purchase order (concrete, structural steel, rebars, MET, fixings) including products certification e.g. Conformité Européene (CE) marks for MET
C14	Information on other construction materials and products (post-installed anchor, acrylic, fixings & aluminium)

Table 2: List of optional data

Form and Data Management

Data standardisation plays an important role in ensuring that the data collected is correct and consistent in terms of formats, structures and conventions. The objective of data standardisation is to maintain data accuracy, ensure the data is usable for analysis, and encourage interoperability across the industry.

This section serves as a guide on the data standards for structured data and documentation storage plan with a list of standard file naming and the directory for filing systems for unstructured data. Users are advised to refer to [Site Management Data Standards](#) for the data standardisation requirements of structured data.

For both unstructured and optional data, vendors should provide customised solutions to store the documents and information in SMP based on the requirements of different system owners.

For unstructured data, the system owner should determine a standardised documentation storage plan to serve as a directory for users to find and store documents. This information may be documented as PDF, images, drawings or MS Word document files. The recommended documentation storage plan for required unstructured data is tabled below. Any source documents to generate the required structured data (e.g. original concrete cube test reports) should also be kept neatly in the SMP for audit purposes.

SN	Document	Description	Example of Folder Name	Directory
1	Pre-construction Survey Report	Pre-construction Survey and relevant documents/photos	BCA >> Pre-con Survey >> [Project Name]	BCA >> Pre-con Survey >> [Project Name]
2	Temporary Building	Temporary Building COS, PE Design, Room Layout Plan etc.	BCA >> Temporary Building >> [Building name]	BCA >> Temporary Building >> Site Office Block A
3	Steel Mill Cert & FPC	All material certificates	BCA >> Certification >> [Cert Name]	BCA >> Certification >> Steel Mill Cert
4	RFI	All RFI forms	BCA >> RFI >> Workstream >> Serial no. Ex: BCA >> RFI_ARCH_001	BCA >> RFI >> ARCH

Workflow and Report Management

Examples of recommended workflow and processes for the dataset are shown below. These recommendations serve as a reference to develop SMPs. Solution providers should work with clients to customise the workflow and processes for each dataset and ensure necessary endorsements are met.

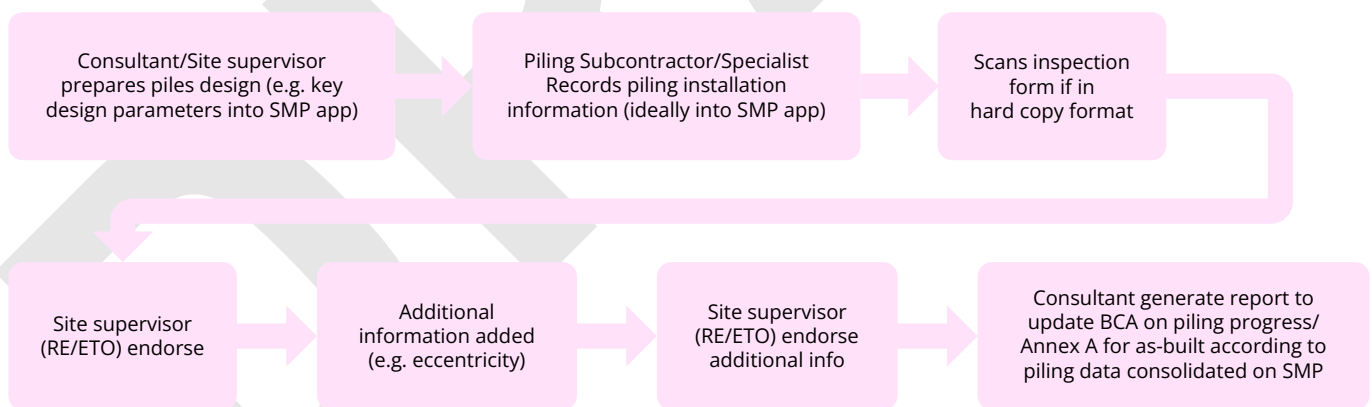


Figure 1: Recommended workflow of piling installation record

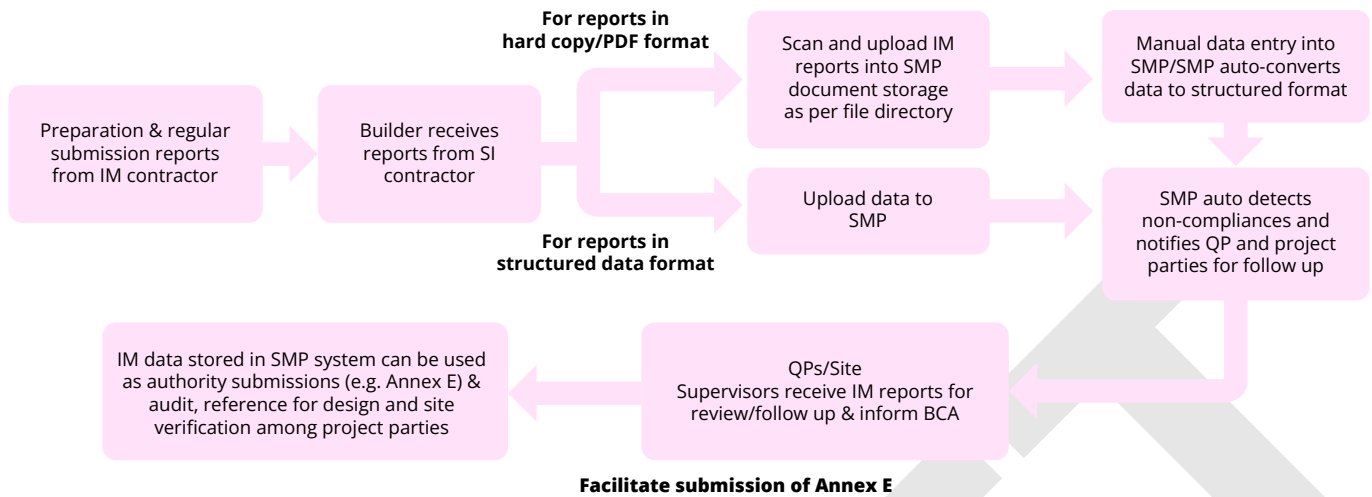


Figure 2: Recommended workflow of Instrumentation and Monitoring record

Essential Functions

The basic functions below are recommended to be included in SMPs. Solution providers should be able to provide these functions when developing the SMP:

- a. Time-based electronic processes to circulate forms and records automatically to designated users.
- b. Issue notifications to designated users according to workflow assignment.
- c. Auto-trigger data and alert authorised users for action on critical issues e.g. material test failure, instrument reading exceeds alert level.
- d. Generate reminders by means of emails/push notifications for events such as overdue/outstanding actions, incomplete workflow processes, data or poor performance etc.

User Management

This section covers the role and responsibilities of authorised users and user access rights.

Solution providers should provide the service requirements listed below:

- a. Allow system owners to assign users based on different user groups, as well as manage and assign different access rights to different users or user groups.
- b. Allow system owners to issue login usernames and passwords to users by email.
- c. Allow users to reset passwords with their registered email and various factor authentications. Given that the data is owned by the Project Team, solution providers should enhance user authentication and security protocols to align with Personal Data Protection Act (PDPA) guidelines.

Smart Site Sensors Management

Smart site sensors refer to sensors equipped with advanced technologies that allow users to monitor and collect data from various aspects of physical sites or locations. These sensors can be deployed in areas such as buildings or industrial facilities to gather information such as structural and environmental conditions, safety and energy usage.

Solution providers are encouraged to provide seamless integration with different smart site sensors available in the market to incorporate with SMPs. For example, smart site sensors that can be integrated with SMPs include 360 Captures and CCTVs with AI capabilities. 360 Captures can enable comprehensive inspections and defect tracking on construction sites by providing immersive views for remote assessment, progress tracking, and collaboration. On the other hand, CCTVs with AI capabilities can be used to automatically detect safety violations, potential hazards, track construction progress, and optimise resource allocation through real-time monitoring and analysis of site activities. These serve as valuable documentation and analysis tools that can enhance efficiency and accuracy in site management.

Accessibility of Other Devices

SMPs are recommended to be accessible by mobile devices to enable workers to refer to plans and record observations on the go, fostering real-time communication and data access. Contractors should ensure the readiness of infrastructure, such as reliable internet connectivity and mobile device support, to facilitate seamless access to the platform, thereby enhancing productivity and collaboration among on-site personnel.



PART 3

OTHER OPERATIONAL REQUIREMENTS

IT Security Requirements

Companies are responsible for the cyber and data security of the SMPs they adopt, as well as the access given to users. It is essential that companies understand potential risks and take appropriate measures to protect their data and systems from cyber threats. If needed, companies can consider engaging a specialist or consulting firm with expertise in cybersecurity to assess risks, provide recommendations, and assist in implementing robust security measures.


Companies may refer to the Infocomm Media Development Authority (IMDA) and Cyber Security Agency of Singapore (CSA) websites for more information.

Companies should also consider adopting SMPs that have the capability to interface seamlessly with other systems if necessary. This allows for future collaborations, data sharing with partners or stakeholders, and the ability to leverage emerging technologies. SMPs that possess inherent interoperability and the potential for smooth integration can enable companies to adapt to evolving needs and future-proof their systems.

Connection to Exchange Platform

The Exchange Platform is an envisioned data sharing solution to facilitate the secure and efficient sharing of data between different project parties that is currently under development. This can include contractors, developers, consultants, government agencies and other organisations. The value of a data exchange platform would shift the industry from complicated webs of data exchange to one where each organisation only requires a single point of connection, all while maintaining data security. With the submission of the same dataset to multiple different parties, the data exchange platform would simplify the connection set-ups required between systems to generate much cost savings.


PRINCIPLES OF THE EXCHANGE PLATFORM

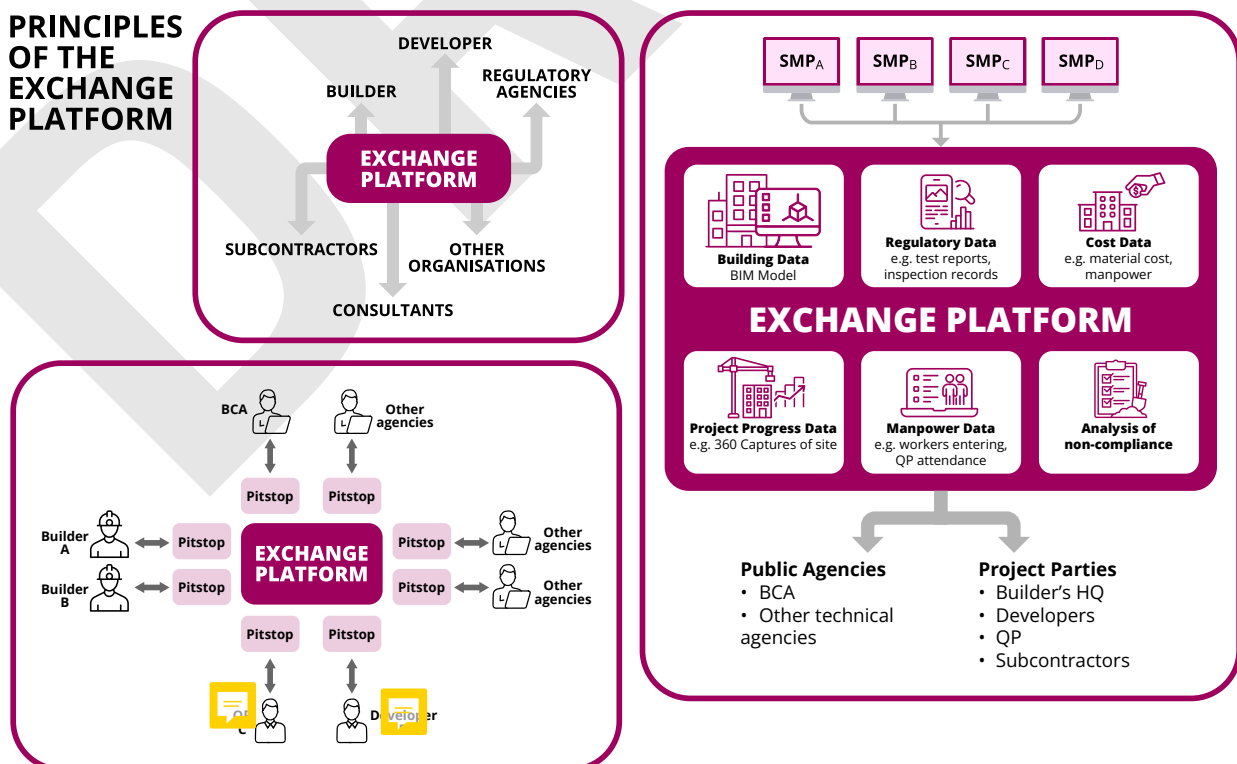

The purpose of the Exchange Platform is for:

1. **Data Sharing:** Enabling seamless and controlled sharing of data between authorised parties, fostering collaboration and innovation.
2. **Data Security:** Provide robust security protocols to protect the confidentiality, integrity, and availability of the shared data, including access controls and monitoring.
3. **Efficiency:** Streamlining the process of data exchange, reducing manual effort, and improving the speed and accuracy of data sharing.
4. **Interoperability:** Standardising common datasets and fields, allowing different systems to communicate and integrate effectively.
5. **Governance and Control:** Providing regulators with direct access to carry out audits.
6. **Collaboration:** Enhance collaboration between project parties by providing the means for sharing real-time project data, facilitating better coordination, decision-making, and transparency across all stakeholders.

Site Management Platforms shall be developed to support API integration with the Exchange Platform for the required data outlined in Chapter 3. In the future when the Exchange Platform has been developed, regulators like BCA can access the data that is required to be audited digitally without going down to the site. Builders can also leverage the Exchange Platform to integrate the different SMP systems that they use, or with other project parties like the systems of their material test labs or their developers.

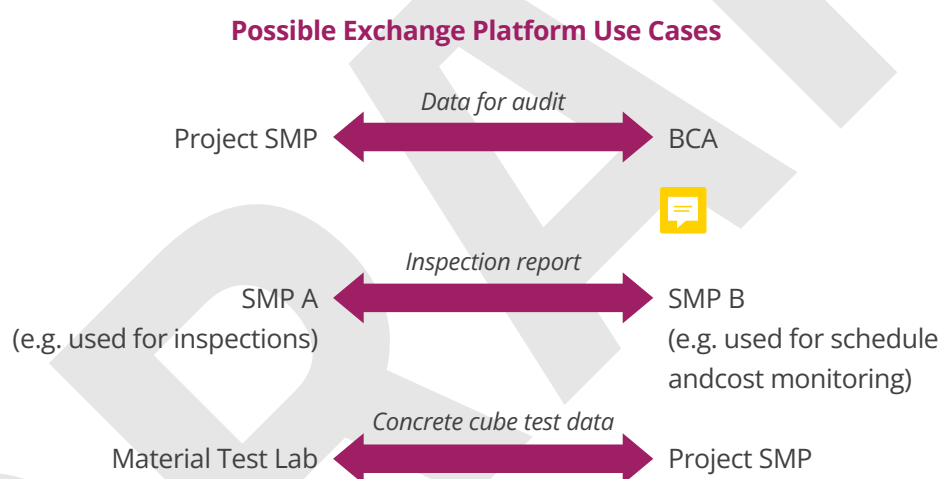

System Maintenance

Regular system maintenance is crucial to prevent downtime and disruptions to site operations. By conducting routine maintenance activities, companies can ensure that their SMPs and associated systems are functioning optimally. This includes tasks such as software updates, hardware checks, data backups, and performance monitoring. Proactive maintenance helps identify and address potential issues before they escalate, minimising the risk of unexpected system failures or downtime. By prioritising system maintenance, companies can maintain the reliability, availability, and performance of their SMPs, ensuring smooth operations and minimising any negative impact on site activities.

Archiving of Data After Project Completion

Data stored on the SMP should be archived and handed over to stakeholders such as the developer to preserve project information. This is to ensure that stakeholders have access to valuable resources for future references, maintenance and potential legal or regulatory requirements.



Feedback

This Guide will be updated progressively from the First Edition published on April 2024. We welcome your comments about this Guide to help us continue to develop and improve it. Please provide your inputs at <https://go.gov.sg/smpguidefeedback> or scan the QR code on the right.

